

Description: Norumbega Covered Storage Tank	Contract No. 6213
Contractor: Norumbega Constructors - J.F. White w/ Slattery-Skanska in association with Metcalf & Eddy	Status as of: December 31, 2004

Major Progress Items:

- Working on punchlist items for Milestones 1&2.
- Continue repair of VV#1 joint.
- Working on Security Modifications CO.
- Placing fill and grading around site.

Safety:

- No incidents reported, 50 total, 3 lost time to date.

QA/QC:

- 37 EARs issued to date, 33 closed.
- Landscaping Issues

Public Affairs:

- Next Weston Working Group meeting – TBD
- Awaiting date from WCC on public hearing.

Schedule Assessment:

The recent schedule submission (W19) updates the project schedule through December 31, 2004. In this month's schedule update, the final completion milestone has been maintained at 16Jun05. This date remains consistent at -229 calendar days past the contractual completion date.

There are a limited number of work activities scheduled between the first of the year and the Spring of 2005. Some of the remaining work include: 1) Cell #3 slope and landscaping, then demo of ramp, and demobilization, 2) install the tank roof drain, 3) complete the dam/spillway road, 4) construct the tower roadway, 5) reset the stone wall, 6) demo the remote parking lot, 7) work in Wetlands E, and 8) complete slope/loam/landscaping at Cell #2 & #1, 9) complete the tank access roadway, 10) loam and seed on the roof. 11) Valve Actuator T&M Change-Out, 12) Punchlist, 13) VV # 1 pipe joint repair.


Cost Summary:

Award Value:	\$89,400,000.00
Previously Executed CO's:	\$5,346,694.76
Previous Contract Value:	\$94,746,694.76
CO's Executed this Month:	\$0.00
Current Contract Value:	\$94,746,694.76*

Payment Summary:

Previous Gross Amount:	\$92,558,768.29
This Month's Gross Amount:	\$11,000.00
Gross Amt. To-Date:	\$92,569,768.29*
Retainage To-Date @ 5%:	\$4,628,488.41
Retainage Release 1:	\$2,657,839.00
Total Payable To-Date:	\$90,599,118.88

Billed to Date (Early Plan; Based on REV5 Recovery Sch)	99.2%
Billed to Date (Late Plan; Based on REV5 Recovery Sch)	99.2%
Billed to Date (Actual - with retainage)*	97.6%

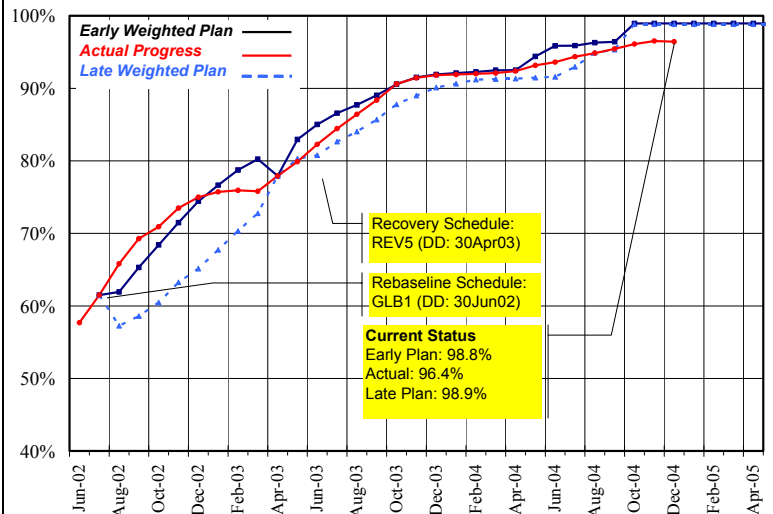


Costs: ↑ **Change Orders:** ↓

Overall D.B. Weighted Physical Progress: ↑

CO No.

24 - Time Extension – 6/30/05

PCO No. None at this time

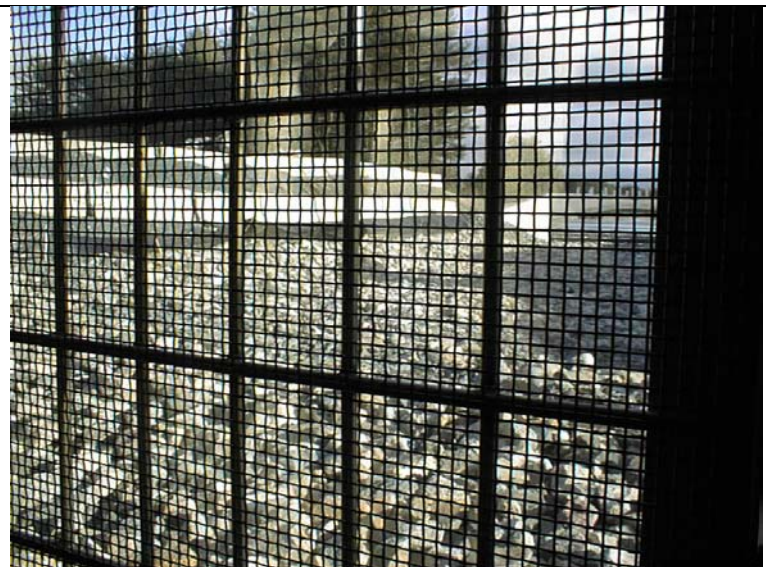

Schedule Review	Contract Required Dates	REV5	W19A	W20A	Variance (Cal Days)		
		Recovery Schedule	Last Month	Current Month	Contract	Rec. Sch.	Last Mnth
Milestone 1 (Act 1040)	10/3/2003	10/3/2003	10/3/2003	10/3/2003	COMPLETED		
Milestone 2 (Act 1049)	8/30/2004	8/26/2004	6/14/2004	6/14/2004	COMPLETED		
Final Accept. (Act.1050)	10/30/2004	10/26/2004	6/16/2005	6/16/2005	-229	-233	0

Schedule Dates: ↑

Completed 1/2" SS Screening at PRF & Spillway: ↑
